LAB 2 – JIRA HANDS-ON

Agile Backlog Creation & Sprint Simulation

Patient Health Record Consent Management System

1. Agile Backlog – Epics and User Stories

The Lab 1 functional requirements were converted into three major Agile themes and nine User Stories, with priorities and Fibonacci estimates.

Epic	User Story	Priority	Points
Epic 1 – Consent Management	Grant Consent	High	5
Epic 1 – Consent Management	Select Medical Records	High	3
Epic 2 – Consent Revocation & History	Revoke Consent	High	5
Epic 2 – Consent Revocation & History	View Consent & Access History	Medium	3
Epic 3 – Medical Record Access & Audit	Request Record Access	Medium	3
Epic 3 – Medical Record Access & Audit	Verify Requester	High	3
Epic 3 – Medical Record Access & Audit	Check Consent Validity	High	3
Epic 3 – Medical Record Access & Audit	Access Medical Records	High	5
Epic 3 – Medical Record Access & Audit	Record Audit Event	High	5

Total backlog estimate: 35 story points.

2. Story Point Assignment – Jira Evidence

The screenshot shows the nine User Stories with Fibonacci estimates of 3 or 5 points.

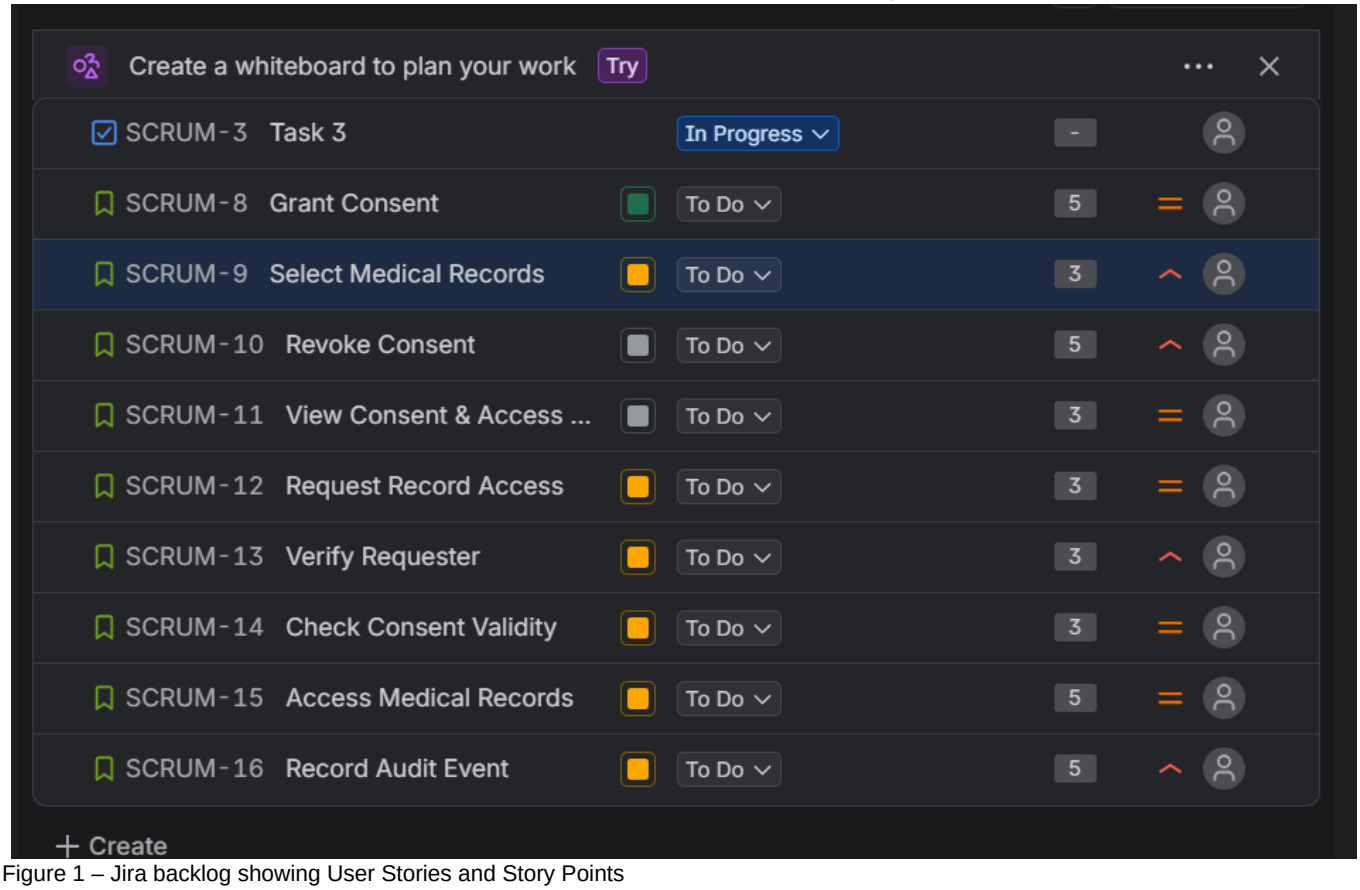


Figure 1 – Jira backlog showing User Stories and Story Points

3. Sprint Board – Active Sprint Evidence

The sprint was simulated using the To Do → In Progress → Done workflow.

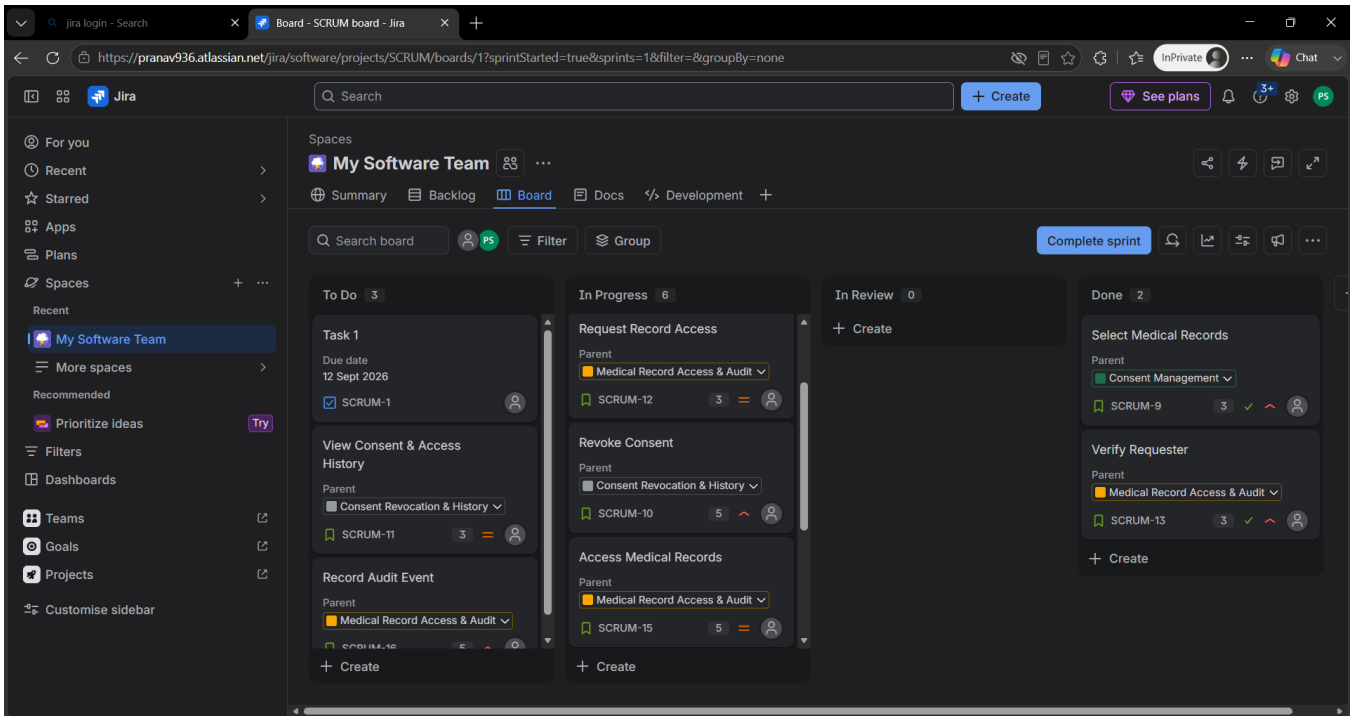


Figure 2 – Jira Active Sprint board during execution

4. Sprint Planning / Commitment Evidence

The second simulated sprint contained five carried-over stories with a 21-point commitment.

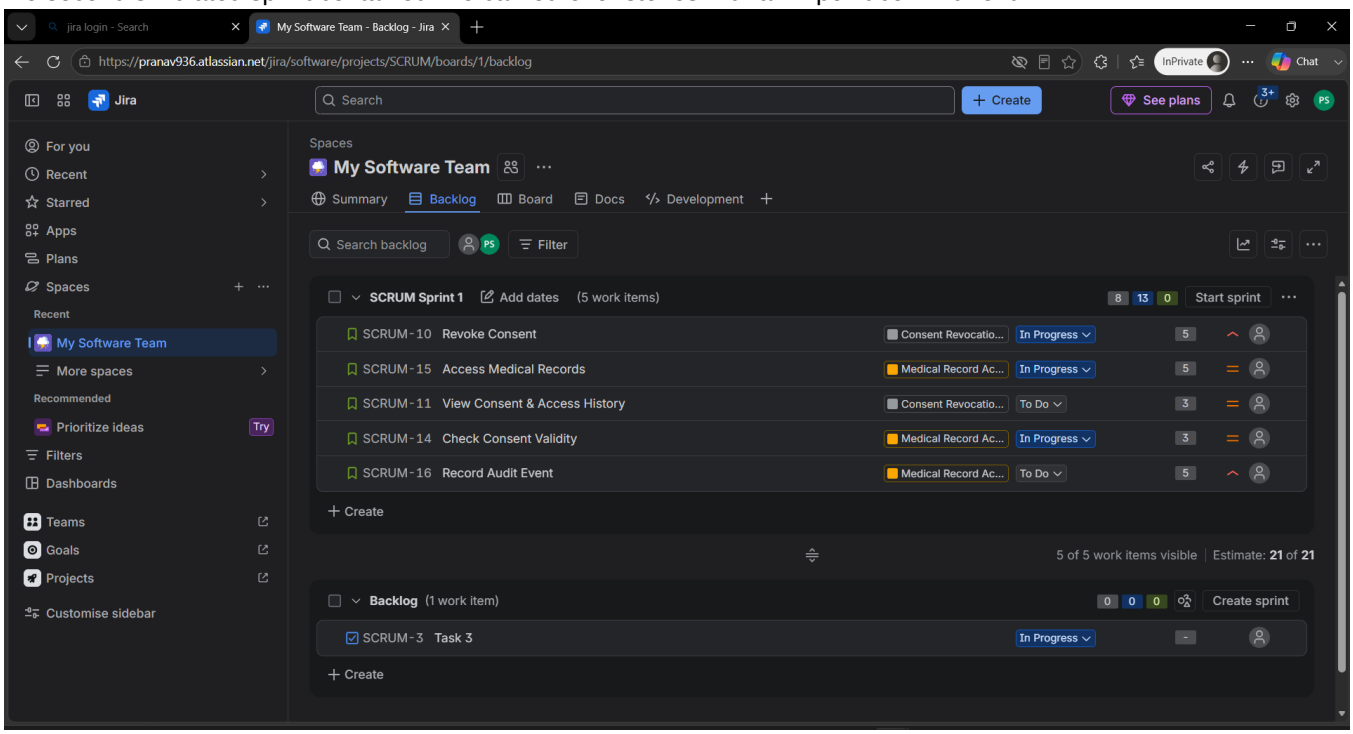


Figure 3 – Sprint planning view showing 5 work items and 21 story points

5. Burndown Chart

The one-week sprint burndown chart starts at 21 story points and reaches 0. The steep drop reflects the simulated completion of several items together.

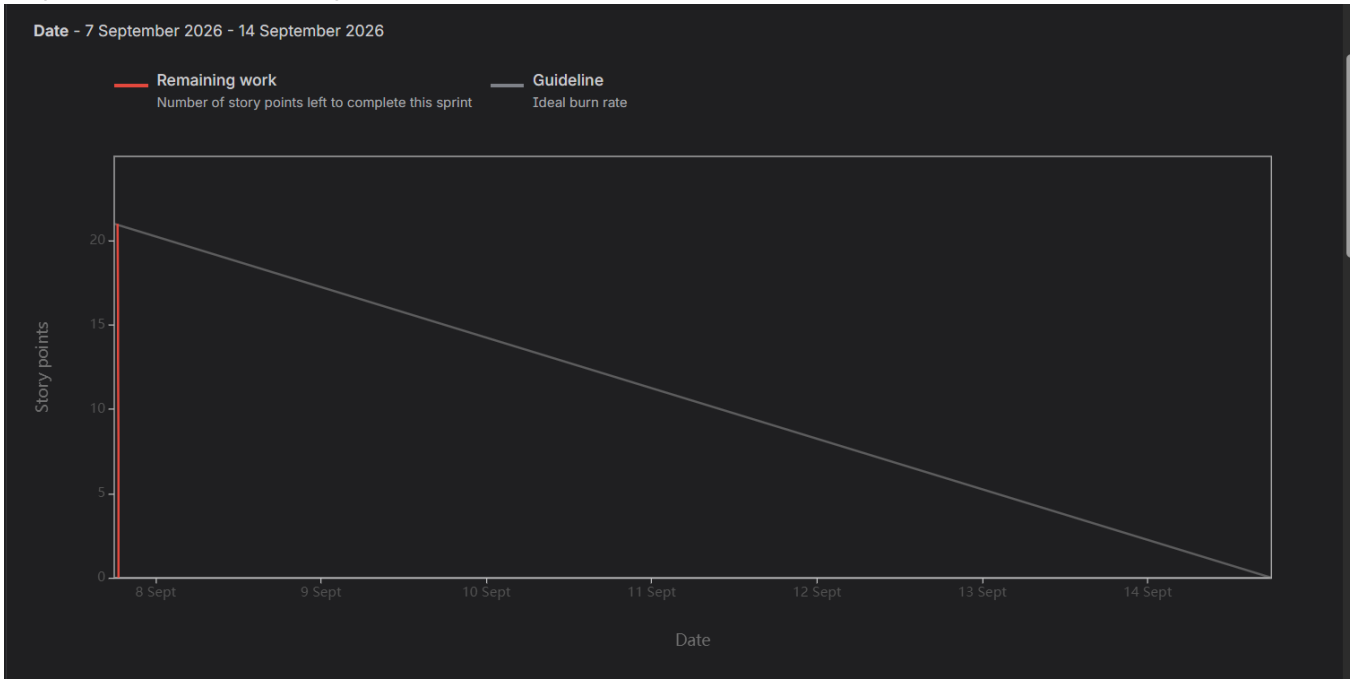


Figure 4 – Jira Sprint Burndown Chart (7–14 September 2026)

6. Reflection Questions

1. Did your estimations reflect the actual effort?

Yes, the estimates were reasonably consistent with the simulated effort. The backlog used Fibonacci values of 3 and 5 points, and the second sprint successfully completed all 21 planned story points. However, because this was a simulation, the estimates cannot be treated as a real-world velocity measurement.

2. Was your backlog well-prioritized?

Yes. High-priority stories were placed ahead of medium-priority stories because they directly support core consent and security functions. Grant Consent, Revoke Consent, Select Medical Records, Verify Requester, Check Consent Validity, Access Medical Records, and Record Audit Event were treated as high priority, while access-request and history features were medium priority.

3. How did your simulated sprint align with your plan?
The sprint followed the planned Scrum workflow: work was selected, the sprint was started for one week, and stories were progressed through To Do, In Progress and Done. The second sprint completed all five carried-over stories, totaling 21 story points.

4. What insights did the burndown chart give about your team's capacity?
The chart showed that the team was able to complete the full 21-point sprint commitment. It also highlighted that the simulation recorded completion in a concentrated period, so the burndown was much steeper than a typical day-by-day sprint. For future sprints, smaller daily updates would give a more realistic view of progress and capacity.

7. Submission Checklist

■ Jira backlog with Epics and User Stories
■ Story point assignments
■ Sprint board – Active Sprint view
■ Sprint Burndown Chart
■ Brief reflection document answering all four questions
